| ID | Task Name | Unit | Duration | Start | Finish | % Complete |
|---|---|---|---|---|---|---|
| 1 | Name of the work : Restoration and Improvements of Roads at Hesaraghatta Main road, G Ramaiah layout, Sai Archade layout, Vijaya bank layout, Adityanagara Phase-02, and Surrounding areas in ward no-03 of Yelahanka New town Sub-division | | | | | 0% |
| 2 | Name of Agency: Sri K Venkataraju. | | | | | 0% |
| 3 | Work Order No: BBMP/EE/YNK.D/EPMT-08/W.O/ Date: 15.02.2022 | | | | | 0% |
| 4 | Mobilization | | 10 days | Tue 15-02-22 | Mon 28-02-22 | 100% |
| 5 | Earthwork Excavation for Drain Work | Cum | 25 days | Sun 20-02-22 | Thu 24-03-22 | 85% |
| 6 | Plain Cement Concrete 1:4:8 | Cum | 35 days | Fri 25-02-22 | Thu 14-04-22 | 89% |
| 7 | TMT Steel | Tonne | 35 days | Sat 05-03-22 | Thu 21-04-22 | 80% |
| 8 | Reinforeced Cement Concrete M20 | Cum | 40 days | Thu 10-03-22 | Wed 04-05-22 | 85% |
| 9 | 100mm Precast Covering Slabs | Sqm | 35 days | Fri 25-03-22 | Thu 12-05-22 | 92% |
| 10 | 230mm Culvert Covering Slab | Sqm | 35 days | Fri 25-03-22 | Thu 12-05-22 | 54% |
| 11 | Plain Cement Concrete 1:3:6 | Cum | 35 days | Mon 28-03-22 | Fri 13-05-22 | 92% |
| 12 | Pre Cast Kerb | Nos | 45 days | Mon 28-03-22 | Fri 27-05-22 | 100% |
| 13 | Earthwork Excavation for Road Work | Cum | 35 days | Tue 15-03-22 | Mon 02-05-22 | 12% |
| 14 | Compaction of original ground | Sqm | 35 days | Sun 20-03-22 | Thu 05-05-22 | 11% |

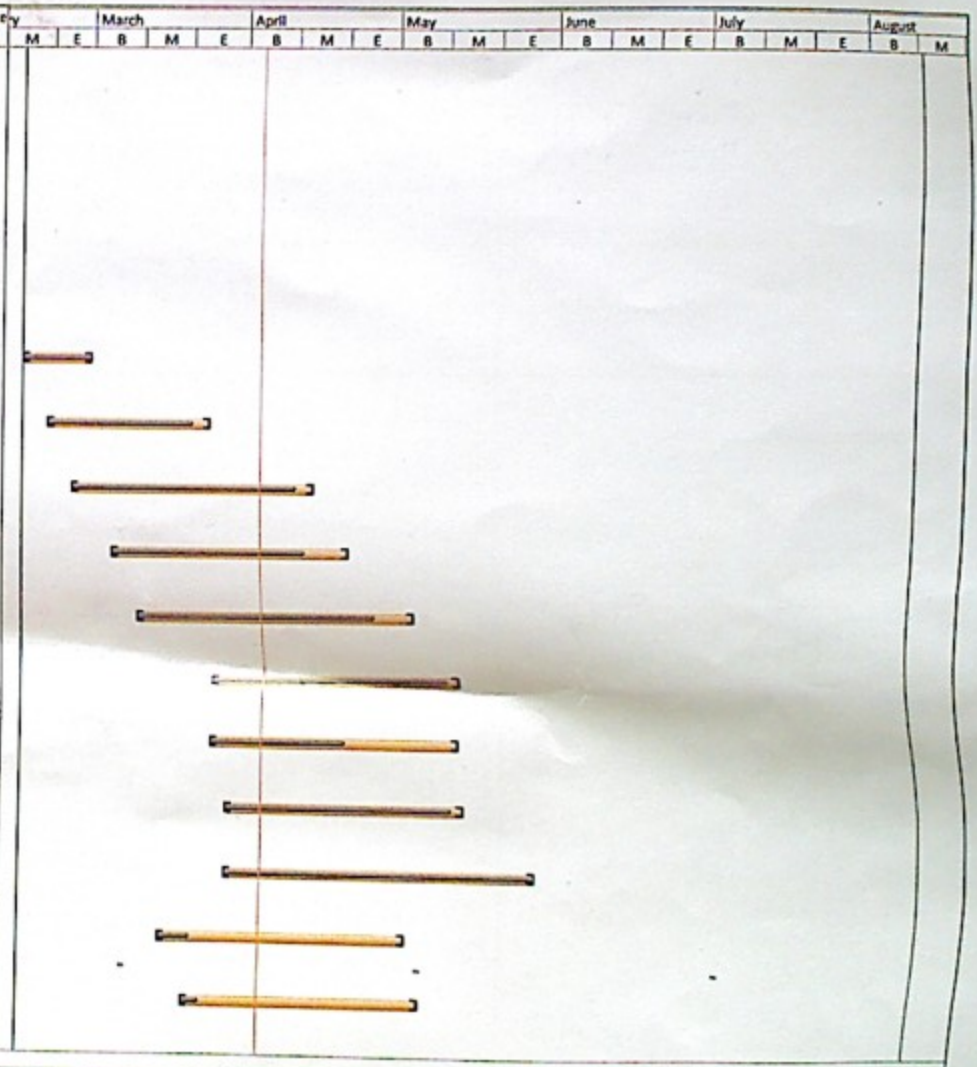


Project: Package-09, Bar Chart
Date: Mon 04-04-22

Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress



ಕರ್ತವ್ಯ ನಿರತ ಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-106

| ID | Task Name | Unit | Duration | Start | Finish | % Complete |
|---|---|---|---|---|---|---|
| 15 | Granular Sub Base | Cum | 50 days | Fri 25-03-22 | Thu 02-06-22 | 15% |
| 16 | Wet Mix Mecadam | Cum | 50 days | Wed 30-03-22 | Tue 07-06-22 | 15% |
| 17 | Primer Coat | Sqm | 55 days | Sun 10-04-22 | Thu 23-06-22 | 15% |
| 18 | Dense Graded Bituminous Macadam | Cum | 70 days | Mon 11-04-22 | Fri 15-07-22 | 15% |
| 19 | Tack Coat | Sqm | 70 days | Tue 12-04-22 | Mon 18-07-22 | 15% |
| 20 | Bitumious Concrete | Cum | 70 days | Wed 13-04-22 | Tue 19-07-22 | 15% |
| 21 | Lane Marking | Sqm | 25 days | Sun 10-07-22 | Thu 11-08-22 | 0% |
| 22 | Pavement Markers or Studds | Nos | 25 days | Sun 10-07-22 | Thu 11-08-22 | 0% |
| 23 | Kerb Painting | Sqm | 30 days | Fri 01-07-22 | Thu 11-08-22 | 93% |

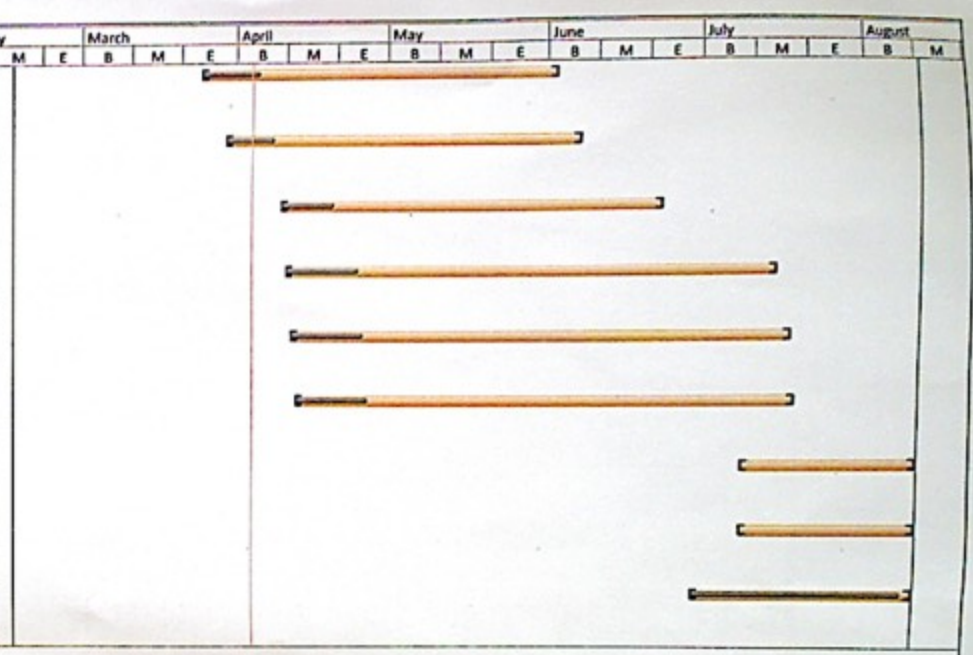


Project: Package-09, Bar Chart
Date: Mon 04-04-22

Task
Split
Milestone
Summary
Project Summary
External Tasks
External Milestone
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
Deadline
Progress



ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಯೋಜನೆಯ ಉಪವಿಭಾಗದ ಅಧಿಕಾರಿಗಳು
ಜಿ.ಜಿ.ಎಂ.ಕೆ. ಬೆಂಗಳೂರು-106
